


ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	2015		2016		2017		2018		2019		2020		2021	
							H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	
1		Siddha Happyville																		
2		AZURE BLOCK																		
3		Foundation Work	689 days	Fri 9/12/14	Sun 7/31/16															
4		Structural Work	731 days	Sun 7/17/16	Tue 7/17/18	3FS-15 days														
5		Finishing Work	340 days	Fri 12/29/17	Mon 12/3/18	4FS-201 days														
6		AQUA BLOCK																		
7		Foundation Work	492 days	Thu 5/28/15	Fri 9/30/16															
8		Structural Work	597 days	Fri 9/16/16	Sat 5/5/18	7FS-15 days														
9		Finishing Work	366 days	Tue 12/12/17	Wed 12/12/18	8FS-145 days														
10		INDIGO BLOCK																		
11		Foundation Work	598 days	Tue 8/12/14	Thu 3/31/16															
12		Structural Work	840 days	Mon 3/7/16	Sun 6/24/18	11FS-25 days														
13		Finishing Work	373 days	Thu 12/14/17	Fri 12/21/18	12FS-193 days														
14		SAPPHIRE BLOCK																		
15		Foundation Work	506 days	Thu 9/4/14	Fri 1/22/16															
16		Structural Work	880 days	Sun 1/3/16	Thu 5/31/18	15FS-20 days														
17		Finishing Work	365 days	Sun 12/31/17	Sun 12/30/18	16FS-152 days														
18		FERN BLOCK																		
19		Foundation Work	786 days	Thu 5/28/15	Fri 7/21/17															
20		Structural Work	883 days	Sat 7/1/17	Sat 11/30/19	19FS-21 days														
21		Finishing Work	302 days	Sat 6/1/19	Sat 3/28/20	20SS+700 days														
22		MINT BLOCK																		
23		Foundation Work	583 days	Tue 5/26/15	Wed 12/28/16															

Project: msproj11 Date: Sun 9/15/19	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Progress	
	Project Summary		Duration-only		Manual Progress	
	External Tasks		Manual Summary Rollup			
	External Milestone		Manual Summary			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	2015		2016		2017		2018		2019		2020		2021	
							H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	
24		Structural Work	1072 days	Wed 12/14/16	Wed 11/20/19	23FS-15 days														
25		Finishing Work	285 days	Mon 6/17/19	Fri 3/27/20	24SS+915 days														
26		CITRON BLOCK																		
27		Foundation Work	587 days	Mon 10/16/17	Sat 5/25/19															
28		Structural Work	421 days	Sun 5/5/19	Sun 6/28/20	27FS-21 days														
29		Finishing Work	397 days	Sun 12/1/19	Thu 12/31/20	28SS+210 days														
30		OLIVE BLOCK																		
31		Foundation Work	229 days	Mon 4/1/19	Fri 11/15/19															
32		Structural Work	300 days	Wed 11/6/19	Mon 8/31/20	31FS-10 days														
33		Finishing Work	585 days	Mon 2/24/20	Thu 9/30/21	32SS+110 days														
34		CLUB HOUSE																		
35		Foundation Work	398 days	Mon 2/2/15	Sat 3/5/16															
36		Structural Work	662 days	Wed 2/3/16	Sat 11/25/17	35FS-32 days														
37		Finishing Work	754 days	Tue 9/12/17	Sat 10/5/19	36FS-75 days														
38		MLCP																		
39		Foundation Work	547 days	Tue 5/29/18	Tue 11/26/19															
40		Structural Work	240 days	Wed 11/6/19	Thu 7/2/20	39FS-21 days														
41		Finishing Work	181 days	Mon 5/4/20	Sat 10/31/20	40FS-60 days														

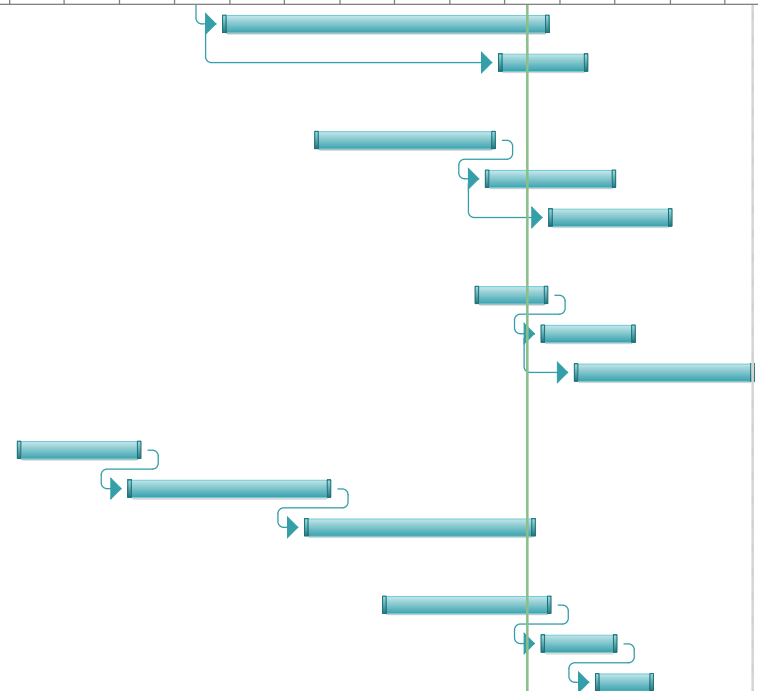

Project: msproj11
Date: Sun 9/15/19

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Progress	
Project Summary		Duration-only		Manual Progress	
External Tasks		Manual Summary Rollup			
External Milestone		Manual Summary			
